



## HCSD Project Update Week Ending May 29, 2015

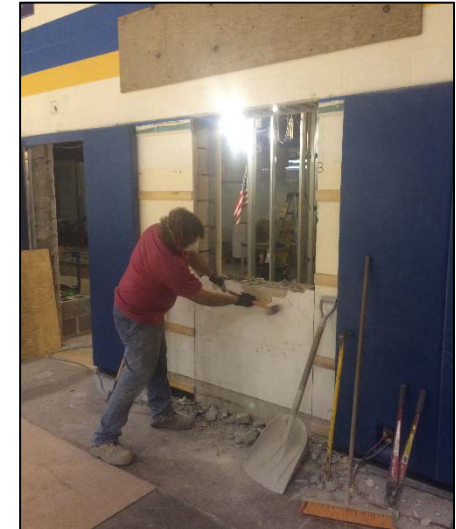

### HS Locker Rooms:

- Masonry block knockout for new doors from gym into locker rooms.
- Bring subbase up to grade in shower/toilet/storage areas.
- Concrete infill at locker/bench bases.
- Installed door frames & framing for partition stalls.
- Removed hard ceiling between girls' locker room and kitchen.
- Masonry block infill old door and ductwork openings into gym.
- Began placing/installing ductwork.
- Plumbing rough-in in boys' toilet room.
- Installed new branch circuit piping.
- In-wall electrical rough-in.

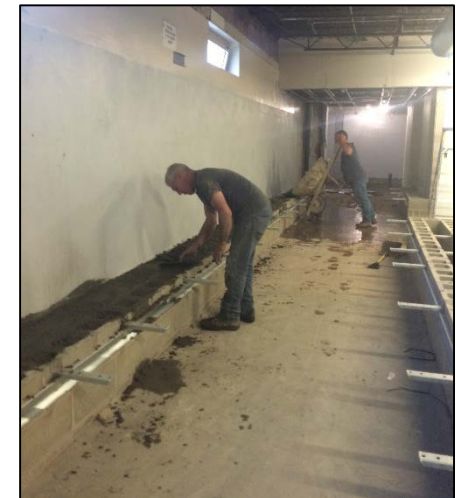

## HCSD Project Update Week Ending May 29, 2015



### HS Art/Tech Wing:

- Excavated trench for additional sanitary line installation.
- Installed 4" pipe in trench with sand bedding.
- Backfilled over installed pipe in trench.
- Prepped trenches with vapor barrier and rebar for concrete pour.
- Demo heating/ductwork and old art room sink.

### HS Music Suite:

- Installed all casework, countertop, and sink in storage room.
- Installed instrument storage cabinet covers and high density sheet music storage.
